


*LA 1 Pile Load Tests are underway*



A 1200 ton jack being set into place to test piling.



Special casings are installed prior to the load test so that storm scour can be accounted for in the pile design.

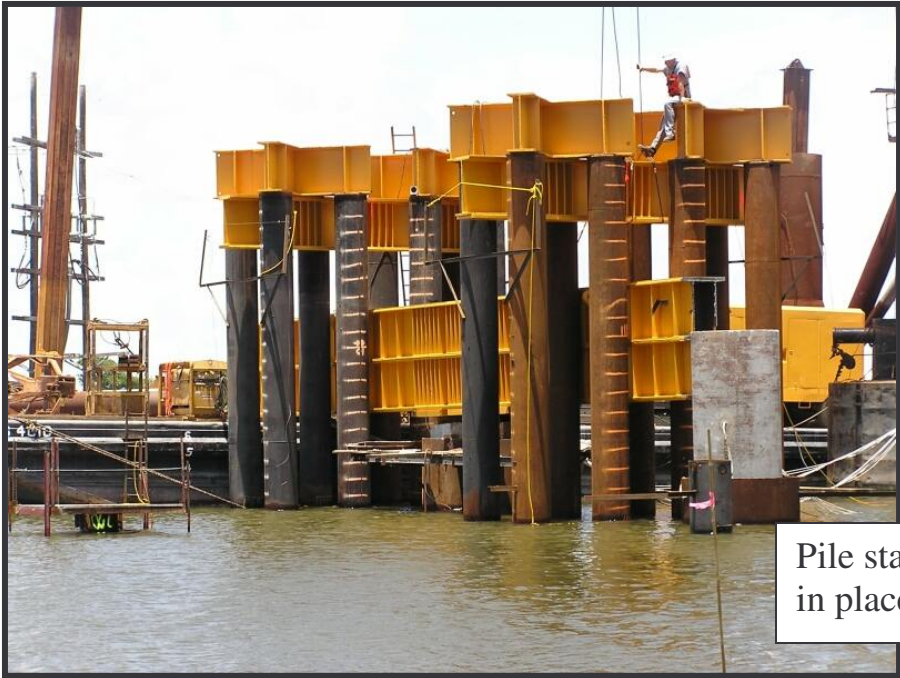

Pile static load test frame is in place and ready for test.



Careful survey control is required to measure pile deflections during the test.
